

Bond Oversight Committee

9/16/25 Meeting #4



Bond Oversight Committee Responsibilities

The BOC is an independent citizens' committee that is responsible to the Superintendent, Board, and general public. The role is to monitor bond-funded construction projects, and help interested citizens stay informed about new construction and renovation projects in the district.

Responsibilities

- To serve as proper oversight and accountability to ensure that bond funds are used as they were intended.
- To provide information to the public on the progress of Bond projects and expenditures of Bond funds.
- To actively monitor all projects and expenditures approved by the voters.
- To report to members of the community on the progress of bond projects.
- To report to the Board on the progress on Bond Projects.
 - Need to select spokespeople to attend and present at Board meetings.

BOC Meeting #4 Agenda

1. Review Updated Program Schedule
2. Bond Budget Update
 - Bond Budget Executive Summary
 - Bond Budget Grand Summary
3. Summer 2025 Work Updates
4. Questions & Next BOC meeting date
5. Board Meeting Presentation




LEGEND	
RFP Selection	Master Planning
Pre-Design	Permits
Design	Pre-Construction
Land Use	Construction
Bid-Award	Closeout



PROJECTS		2024												2025												2026												2027											
		M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D				
1	RFP Architect																																																
	Selection	COMPLETE																																															
2	RFP CM/GC (BHS & AUX GYM)																																																
	Selection	COMPLETE																																															
3	RFP Geotech/Survey																																																
	Selection	COMPLETE																																															
4	Master Planning																																																
	Process	<div></div>																																															
5	Auxiliary Gym																																																
	Pre-Design / Design / Bid-Award	<div></div>																																															
	Permits / Construction / Closeout	<div></div>																																															
6	Banks HS Improvements																																																
	Pre-Design / Design / Bid-Award	<div></div>																																															
	Permits / Construction / Closeout	<div></div>																																															
7	Traffic Circulation Improvements																																																
	Construction	<div></div>																																															
8	Safety & Security Projects																																																
	Security Vestibules / Camera Cabling	<div></div>																																															
	Other Security Projects (Fencing, Cameras)	<div></div>																																															
9	District Maintenance Projects																																																
	Banks ES Roof	<div></div>																																															
	Banks ES HVAC	<div></div>																																															

Summer 2025 Projects - BHS

6/16/2025

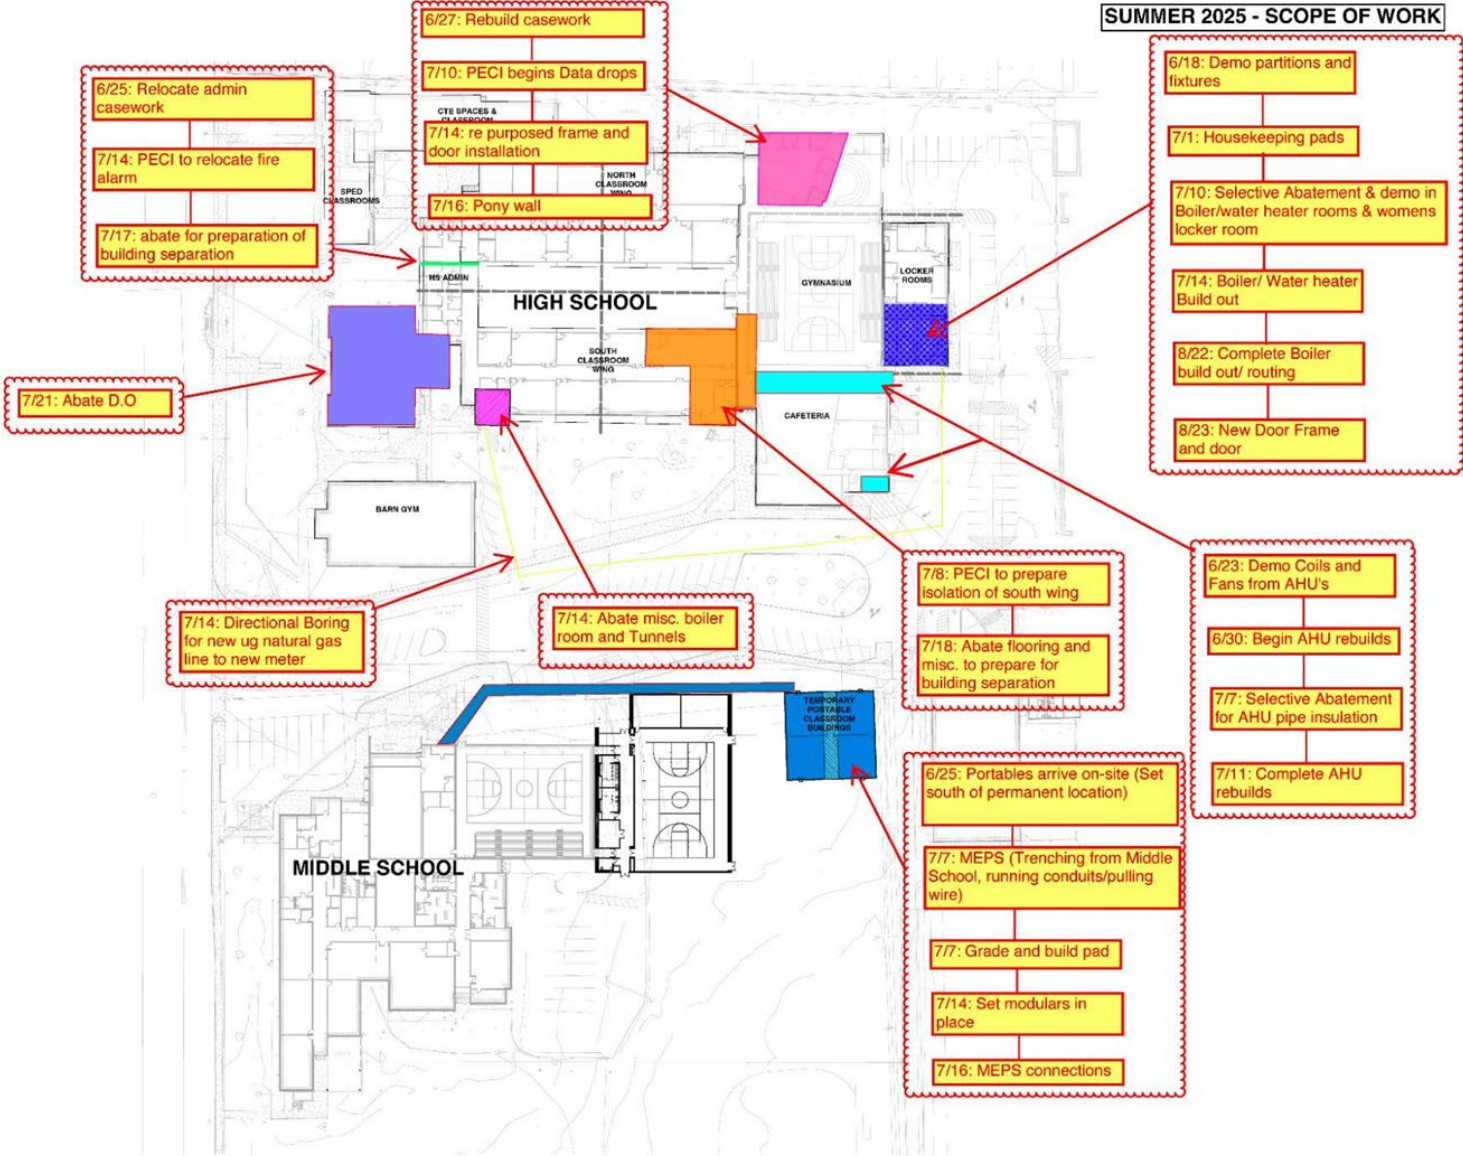

Summer 2025 Projects

Boiler Room Before and After Abatement work



Summer 2025 Projects

Banks High School Abatement (prep for Phase 1 Demo work)



Summer 2025 Projects

District Office Demo & Abatement (prep for Phase 1 Demo work)


Abatement included Bathroom Flooring. Carpet/Mastic. Wall



Summer 2025 Projects

New BHS Gym & Cafeteria Boiler and Water Heater


Rebuilt and Re-fed Gym, Stage & Cafe AHU's (cafeteria has heat!)

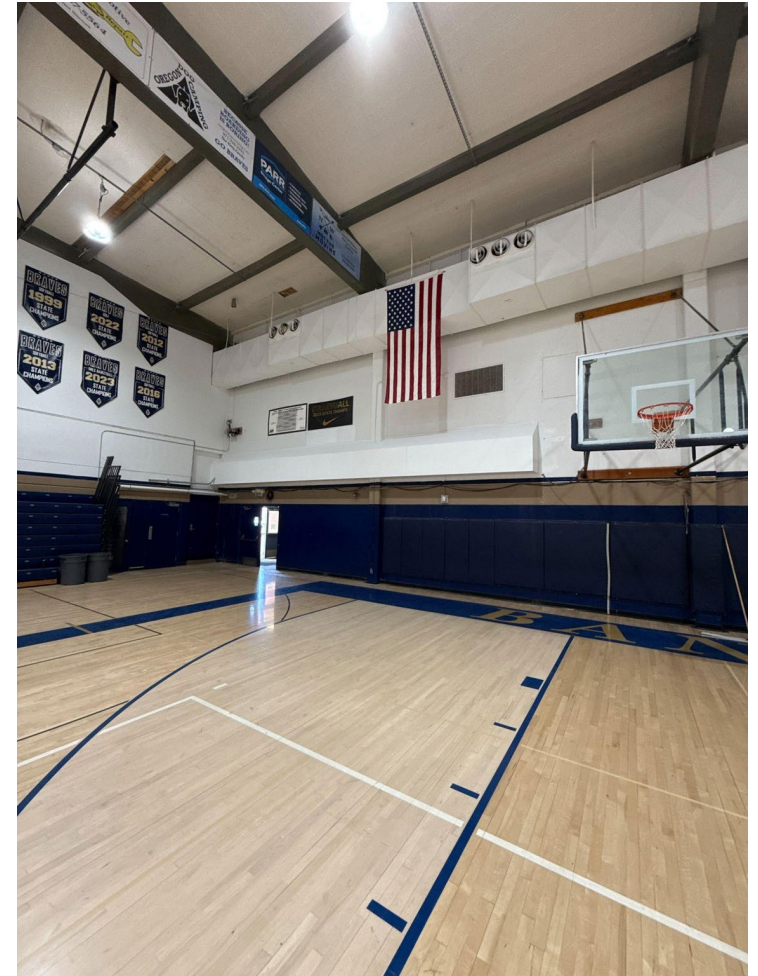

Summer 2025 Projects

Gas Line and Water relocated.

HVAC, Elec, FA, Low Volt relocated for Phase 1 Demo

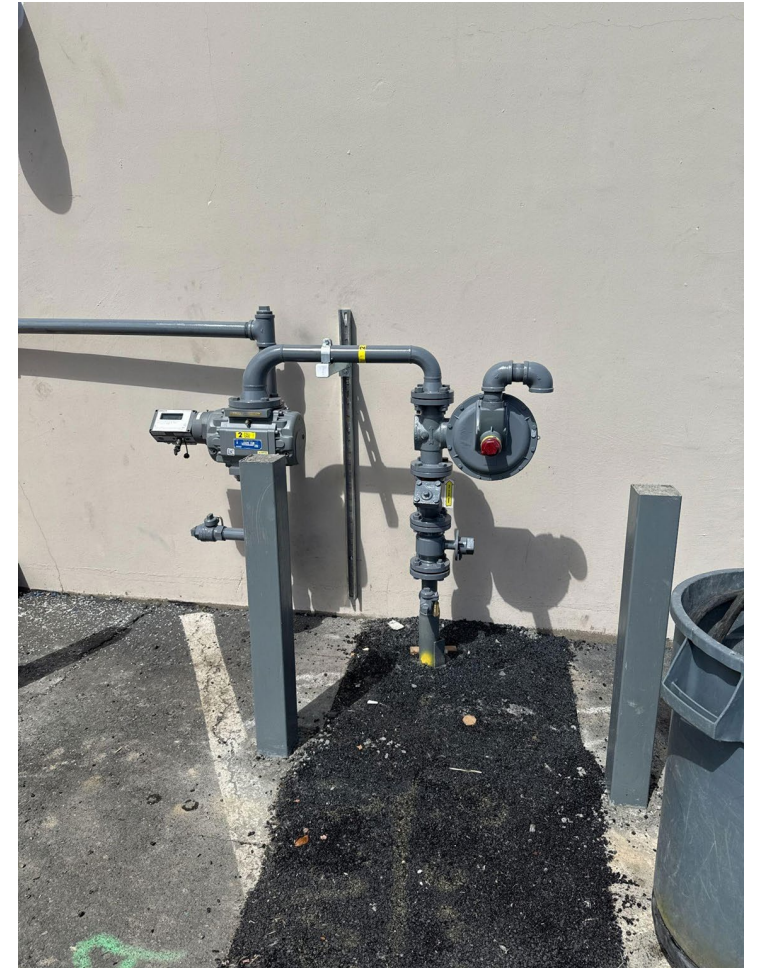

Summer 2025 Projects


Fiber Line relocation from Banks MS to Banks HS

BHS Administration Office relocated



Summer 2025 Projects

Banks MS and Banks ES Secure Vestibules

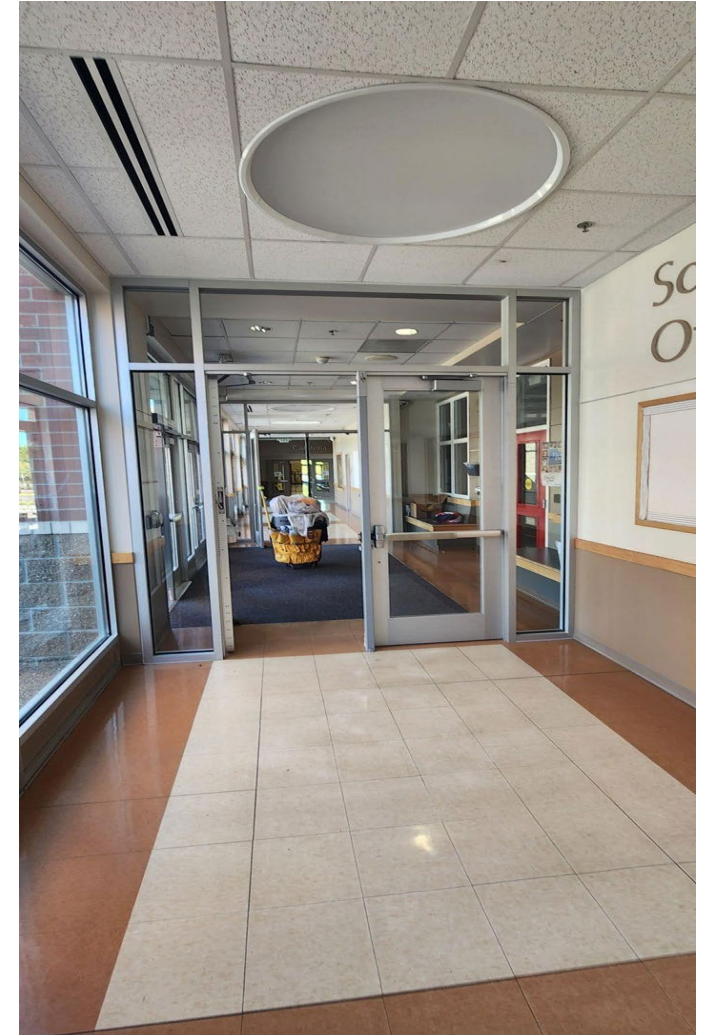

BOC Next Steps

Board Presentation

Next BOC Meeting
